

Sprint 7 Team Lead Report — Dua LEAPa

Oct 1, 2026 · Soli Ateefa, Team Lead

Sprint 7 delivered 25 story points, up 39% on Sprint 6, and moved 11 of the 18 BRS requirements forward. The headline figures are below; the evidence behind each one is in the Appendix section at the end of this report.

Sprint 7 at a glance

Measure	Sprint 7	Context
Story points completed	25	Up 39% from 18 in Sprint 6; 10 more points in review
BRS requirements advanced	11 of 18	BR-01 to BR-05, BR-07, BR-09, BR-10, BR-12, BR-13, BR-15
Automated tests on main	957	Up 47% from 649 a week earlier
Statement coverage	91.6–99.1% per service	Target 60%; builds fail below 70%
PRs merged to main	12 in 4 days	11 in all of Sprint 6

Team lead notes


- **Planning:** I worked with our scrum master, Chris, and the team to split Sprint 7, so stories depended less on each other, after dependencies slowed Sprint 6. Each member took one scrum story and one priority story, focused on the auth service cleanup, OpenAPI docs, Kafka and clearing build warnings. We worked through the carry-over by Wednesday.
- **Capacity:** With the carry-over closed early, the team pulled in five more stories, each discussed and approved. The reporting service was a deliberate priority shift: it is our next major microservice and holds the trade records the BRS requires.
- **Communication:** We held three 30-minute stand-ups, Monday to Wednesday, and asked everyone to document more, so stories don't overlap. Sean, as scribe, records every decision in our Microsoft Teams notes.
- **Reviews:** We match work to each member's strengths. First reviews go to members with fewer commits that week and second reviews to whoever is next in expertise, so knowledge spreads and main stays correct.
- **Improving in Sprint 8:** We are tightening two habits. Every commit message will name its Jira story, and a story moves to In Review only once its PR is open, so the board always matches the code.

Story points by sprint

Sprint 7 completed 25 story points, up from 18 in Sprint 6

Story points done per sprint, from the Jira sprint reports

Story points

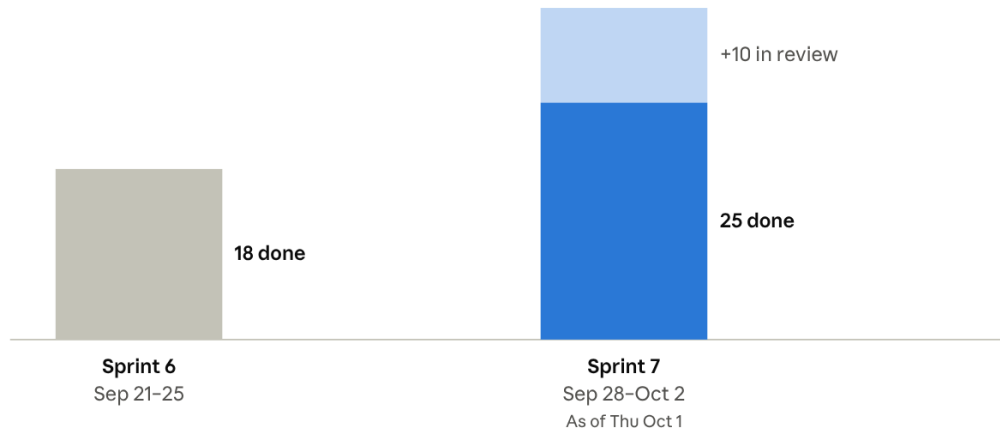

Jira sprint reports (DUA board, KAN board) and KAN resolution dates (pulled Oct 1, 2026)

Sprint 7 also took on five stories pulled in mid-sprint, two of which are already done.

Evidence for your Sprint 7 checklist

The evidence behind each item on your checklist, for your assessment.

Checklist item	Evidence
Story points completed, backlog moves, story completeness	25 points done and 10 in review; 1 story returned to the backlog; all 12 stories have acceptance criteria and 10 sit under a BRS epic
Unit tests for completed Java code	433 JUnit tests: 290 in Holdings and Trade, 143 in Order and Sell
Angular spec tests	310 Vitest specs in 22 files for the client UI
Spring Boot / REST API tests	7 controller integration test classes; order tests post a buy and a sell to /api/orders and check fills, cash, holdings and the audit trail
Integration tests across components	61 Playwright browser tests run in Jenkins; market-data integration tests run against a real Postgres database
Test coverage (60%)	Statement coverage of 91.6% to 99.1% across the four services; builds fail below 70%, or 85% for Holdings and Trade

Checklist item	Evidence
Spot code check (Javadoc, lint)	Javadoc on all 118 main Java files, published in docs/JAVA_DOCS; oxlint on the auth service
PRs for feature branches	12 PRs merged this sprint, 9 by a teammate other than the author; 9 of 12 branch names carry a Jira key
Updated README (architecture, ERD link)	Updated Oct 1 with team roles; includes the service map, an inline ERD and links to every reference doc
Clean Jenkins run (main, docker ps)	Five test stages run in parallel, publish JUnit results and print docker ps
Security (code, PII, data, npm warnings)	No real keys in the repo; RS256 tokens with refresh rotation, rate limiting, lockout after 3 failed sign-ins, inactivity sign-out and account and order reads scoped to the signed-in user; a Playwright spec checks for exposed sensitive data; npm audit fix applied in DUA-67
Architecture (code size, processes, microservices)	4 services plus Postgres and Kafka in Docker Compose, about 19,700 lines of application code
UML and ERD diagrams	Mermaid ERD, service topology, auth class and sequence diagrams
Kafka event bus (extra)	KRaft broker and trade-events topic (3 partitions) in the local and Jenkins stacks

Sprint 8 Plan

Story	Pts	BRS requirement	Why now
DUA-64 OpenAPI Swagger Docs (carry-over)	3	\$10 extensibility	Already started
DUA-29 Align account access with BRS identity rules (carry-over)	2	BR-03	Removes logic the BRS does not ask for
DUA-70 Remove UI Library (carry-over)	5	Maintainability	Already scoped with acceptance criteria
DUA-65 Publish and consume trade events through Kafka	5	BR-07, BR-15	Connects the services to the trade-events topic
DUA-37 Order statuses	2	BR-07	Pairs with the Kafka events
DUA-38 Viewing Order History	5	BR-11	Next must-have in the BRS
DUA-35 Reporting UI	5	BR-16, BR-17	Builds on DUA-34's reporting service
Total	27		Leaves room for carry-over

Appendix: Sprint 7 supporting detail


The evidence behind each number in the Sprint 7 report, for reference: the GitHub trend, story-by-story status, team practices, and how each figure was measured.

Delivery and quality trend, Sprints 1–7


Test cases on main reached 957 in Sprint 7, up 47% on Sprint 6

From Sprint 3 on, merged PRs held at 10–18 a sprint while the test suite grew; Sprint 7 counted through Thu Oct 1

PRs merged into main

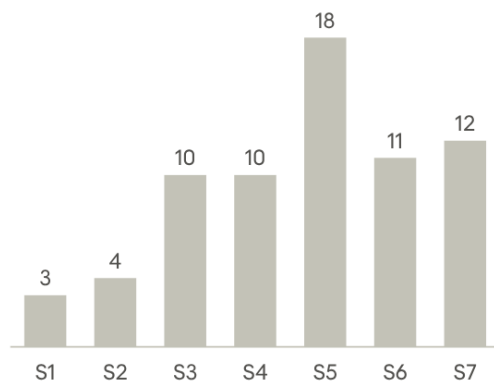

Test cases on main at sprint end

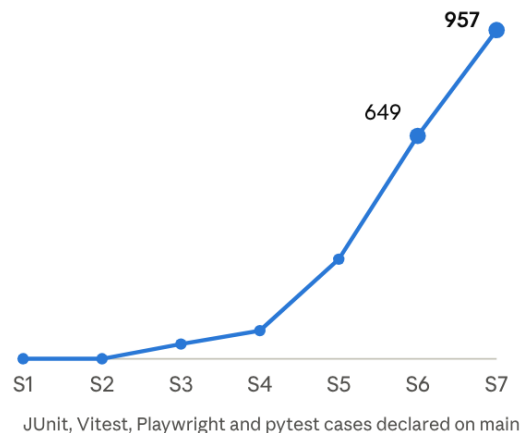

GitHub, merge commits and test declarations on main (Aug 17 – Oct 1, 2026)

Sprint 7 merged 12 PRs in four days against 11 in all of Sprint 6 and added 308 test cases.

Sprint 7 stories

The sprint started Monday with 7 stories (28 points); 5 stories (17 points) were pulled in mid-week, for a final scope of 12 stories and 45 points. Of the Monday plan, 20 of 28 points (71%) are done.

Story	Owner	Pts	Status	BRS link	Evidence
DUA-32 API for Buy/Sell Order	Soli Ateefa	5	Done	BR-04, BR-05, BR-09	PR #73, #74
DUA-61 Auth Service Cleanup	Mohammed Shoaib	5	Done	BR-01, BR-03	PR #75
DUA-42 Mock Data – UI Fullscreen	Chris Chang	5	Done	BR-12, BR-13	PR #77
DUA-54 New User Dashboard View	Prisca Olose	3	Done	BR-02, BR-10	PR #79

Story	Owner	Pts	Status	BRS link	Evidence
DUA-66 Stand up Kafka and the trade-events topic (added Tue)	Mohammed Shoaib	3	Done	BR-07, BR-15 (foundation)	PR #80
DUA-58 Microservice Restructure Documentation	Soli Ateefa	2	Done	BRS §11 architecture rationale	PR #67
DUA-67 Sprint 7 Cleanup (added Tue at your request)	Sean Cheema, Soli Ateefa	2	Done	Checklist: Jenkins, README	PR #81
DUA-63 Buy Sell Order Integration	Sean Cheema	5	In review	BR-04, BR-09	Branch feat/DUA-63, 7 commits
DUA-34 Reporting Service Data Organization (added Wed)	Soli Ateefa	5	In review	BR-16	PR #82, 76% coverage
DUA-64 OpenAPI Swagger Docs	Prisca Olose	3	In progress	Supports BRS §10 extensibility	Branch feat/DUA-2/DUA-64
DUA-29 Align account access with BRS identity rules (added Thu)	Mohammed Shoaib	2	To do	BR-03	Planned
DUA-70 Remove UI Library (added Thu)	Sean Cheema	5	To do	Maintainability	Planned

DUA-68 Legal Trade Regulations (5 points, BR-14) was added Tuesday and moved back to the backlog Wednesday. Every story has acceptance criteria, and 10 of 12 sit under a BRS epic.

How the work was done

All five team members committed code in each of the last three sprints, and three in four pull requests were merged by someone other than their main author.

Measure	Sprint 5 (Sep 14–18)	Sprint 6 (Sep 21–25)	Sprint 7 (Sep 28–Oct 1)
Commits, all branches	84	131	117 (4 days)
Team members committing	5 of 5	5 of 5	5 of 5

Measure	Sprint 5 (Sep 14–18)	Sprint 6 (Sep 21–25)	Sprint 7 (Sep 28–Oct 1)
PRs merged by a teammate, not the author	15 of 18 (83%)	9 of 11 (82%)	9 of 12 (75%)
PR branches named with a Jira key	13 of 18 (72%)	7 of 11 (64%)	9 of 12 (75%)
Stories moved back to the backlog	not tracked	1 (unestimated)	1 (5 pts)

Sprint 7's commit count covers four working days against Sprint 6's five.

Sources

- **Jira:** DUA Sprint 7 and KAN Sprint 6 sprint reports pulled Oct 1. BRS requirements advanced are the BR links on the seven stories done.
- **GitHub:** seankcheema/trading-season history and docs/coverage/README.md, pulled Oct 1.
